Greecon
SH.P.K


H

SITE PACK H

Hotel or guesthouse

Water, solar and grid. Everything for one kind of site in one pack: what to buy, the survey, the diagrams, install day step by step, the platform steps, the commissioning tests and the handover sheet.

FOR	The project manager at this kind of site, the electrician, and the customer's owner at handover
PRINT	The whole pack, for the site in front of you. Tick the boxes as you go
COVERS	Bill of materials · survey · system, wiring, network and enclosure diagrams · install day · numbers, addresses and ranges · the twelve setup steps · commissioning · handover



Version 1.0 · 1 November 2026

Greecon Sh.p.k · Durana Tech Park · info@greecon.earth

Contents

Site pack H Hotel or guesthouse 3
At a glance 3
How to read this pack 4
What it measures 5
What to buy and bring 5
The project manager brings 6
Survey 7
Ask, in this order 7
Look at, and photograph 7
Survey form 8
The drawings 9
At the office 13
In Greecon 13
The box on your desk 14
The numbers and the converter 14
Install day 16
Numbers, addresses and ranges 17
The numbers on the cable 17
The Eastron meters and the pump contact module 17
The ranges on the labels 18
The platform's setup list 18
Step 1 Order form signed and data terms agreed 19
Step 2 Prices from the customer's bills 19
Step 3 Install the box 20
Step 4 Where each device is on the network 21
Step 5 Which register holds which reading 22
Step 6 Every device answers the box 22
Step 7 Readings arrive and look right 23
Step 8 Someone is told when the site needs attention 23
Step 9 Grid meter direction checked 24
Step 10 Alert limits agreed with the customer 24
Step 11 Electrical work done by a licensed electrician 24
Step 12 Commissioned 25
Commissioning 26
Handover 28
Handover record 29
The three most likely problems 30

SITE PACK H

Hotel or guesthouse

Water, solar and grid. A complete pack for one kind of site, in the order of the work: what to buy, the survey, the drawings, the office, install day step by step, the platform's setup list, the commissioning tests and the handover. Print all of it and tick the boxes as you go. The electrician does everything on the mains side; you do the low voltage and the software; Greecon only reads.

At a glance

WHO IT SUITS
A hotel or guesthouse with a water tank and a pump, solar on the roof and a grid connection. The usual first site.

WHAT IT MEASURES
The grid (import and export), the solar production, the tank, the line pressure, the pump's flow (with a flow meter) and whether the pump runs.

PLANNING ESTIMATE
About EUR 800 to 1,800; typically 1,100 to 1,300. Add the electrician's time (half a day to a day) and yours.

TIME
Survey about 1 hour. Install day 4 to 6 hours with the electrician. Commissioning about 1 hour. Handover 30 minutes.

TEMPLATE IN THE PLATFORM
Hotel or guesthouse

STANDARD SETTINGS
Unit numbers: grid meter 1, solar meter 2, water module 3, pump contact module 5 (if the starter has a spare contact). 9600 baud, 8 data bits, no parity, 1 stop bit. Converter on port 502, in Modbus TCP to RTU gateway mode. All set at the office.

The order of the work: survey, buy, prepare at the office, install day, the platform's setup list, commissioning, handover. Then the morning check, and the day 1, 3 and 7 calls.

STOP

Six rules for the whole job.

1. **Greecon only reads.** It measures; it never switches anything. Never connect a wire from Greecon's equipment to a pump starter, an inverter's control, a valve or any safety circuit.
2. **Anything inside a distribution board is the electrician's work,** under the customer's lock-out procedure, with the project manager watching and writing it down. Nobody works on a live conductor.
3. **The project manager does the low-voltage and software side only:** the box, the network, the converter, the data cable (run to the board; the electrician connects its ends at the meters, because their terminals are inside the board), the labels, and the 12 or 24 V supply from a plug-in supply. The electrician wires the 4 to 20 mA loops, with their 24 V supply, as the module's manual draws it.
4. **Never touch the solar panels' wiring (DC), a tank you must climb into, wastewater or chemicals.** The customer's own staff or installer does that. If the only place for a sensor is there, say it is not possible and write why.
5. **Greecon is not a safety system.** The protection already in the customer's equipment (float switches, relief valves, trips) stays the safety layer.
6. **Write everything down at the time.** Photograph every meter's label and display, the wiring before the board is closed, the converter's settings and the box's label.

How to read this pack

Mark	What it means
ELECTRICIAN	The electrician. Everything inside a distribution board, every current clamp and voltage tap, the pump's run contact, and the 4 to 20 mA loops.
PROJECT MANAGER	The project manager: low voltage and software.
CUSTOMER	The customer: access, people, and starting or stopping their own equipment.
☐	A box to tick when it is done. Print the pack and tick as you go.
Do, **Check**, **Stop**, **Tip**, **Say**	The shaded boxes: do this; check this; stop and call the electrician; a useful habit; words to say to the customer.
Figure H-1 and so on	Drawings of this kit. Every drawing is marked with the kit it is for. Terminal numbers are never drawn: follow the maker's manual.

What it measures

The template **Hotel or guesthouse** makes four devices. What each gives:

Reading in Greecon	Comes from	Unit	Standard alert limits
Grid import and **Grid export**	Grid meter: an Eastron SDM630 where the supply enters, unit 1. One meter gives both: positive power is energy coming in, negative is energy sent out	kW	None
Solar production	Solar meter: an Eastron SDM630 on the inverter's AC output, unit 2	kW	None
Tank level	Water I/O module, unit 3: the level transmitter's 4 to 20 mA	%	Critical below 15 % (Act now); Low below 35 % (Check today)
Line pressure	Water I/O module, unit 3: the pressure transmitter's 4 to 20 mA	bar	None
Pump flow	Water I/O module, unit 3: the flow meter's 4 to 20 mA (optional)	litres a minute	No flow at or below 0.2 litres a minute (Act now, once it has held for 30 seconds, and only when the box reads both a flow and the pump's running state)
Pump running	Pump contact module (optional), unit 5: the pump starter's spare contact	on or off	None

Without the flow meter, or without the pump's running contact, "the pump is running but no water is flowing" cannot be raised, and the handover should say so. Solar surplus has no standard limit: the platform says nothing about it rather than guess.

What to buy and bring

	Item	Specification	Qty	Planning estimate (EUR)
☐	**Box**	Fanless x86 mini PC (see the box specification), 8 GB, 128 GB or more SSD or eMMC, 12 to 24 V DC input	1	180 to 300
☐	**Converter**	RS-485 to Ethernet, DIN rail, 9 to 36 V DC, Modbus TCP to RTU gateway mode	1	30 to 60 (basic) or 250 and up (industrial)
☐	**Three-phase meter**	Eastron SDM630 Modbus. The MCT version comes with three clamp-on current sensors for up to 100 A a phase; for more than 100 A, the ordinary SDM630 with 5 A current transformers. *One at the grid connection, one on the inverter's AC output.*	2	90 to 180 each
☐	**4 to 20 mA input module**	Waveshare Modbus RTU Analog Input 8CH (current version, the one that reads current), 8 inputs, 4 to 20 mA, 7 to 36 V DC	1	30 to 60

	Item	Specification	Qty	Planning estimate (EUR)
☐	**Pump contact module**	Waveshare Modbus RTU IO 8CH: eight isolated digital inputs, a dry contact is enough. Relay outputs never used. *Leave it out if the starter has no spare running contact.*	1	30 to 60
☐	**Level transmitter**	Submersible, vented cable, 4 to 20 mA, range at least the tank's height, wetted parts approved for drinking water (or a non-contact ultrasonic sensor above the tank)	1	120 to 400
☐	**Pressure transmitter**	4 to 20 mA, range to suit the pipe (0 to 10 bar is usual), stainless wetted parts	1	40 to 150
☐	**Flow meter** *(optional)*	4 to 20 mA output. Needed for "the pump is running but no water is flowing". *Needed for the no-flow alert.*	0 or 1	150 to 500
☐	**24 V DIN power supply**	30 to 60 W	1	25 to 50
☐	**UPS**	A 12 V DC UPS for the box and converter, or a 600 VA line-interactive UPS	1	60 to 150
☐	**Enclosure and fittings**	IP54 (IP65 outdoors), DIN rail, terminals, fuses or small breakers for the meters' voltage taps, glands	1	80 to 150
☐	**Cable and labels**	Shielded twisted pair for the RS-485 line, network patch cords, ferrules, labels	1 lot	40 to 80
☐	**Cellular router** *(optional)*	4G, DIN rail, data SIM. *Only without usable internet.*	0 or 1	150 to 200

About EUR 800 to 1,800; typically 1,100 to 1,300. Add the electrician's time (half a day to a day) and yours. Ask three suppliers for the quote on the specification, not the brand, and keep the quotes. Buy and bench-test one kit before buying five. The reasons for each part, its settings and the mistakes to avoid are in the Hardware Reference (PDF 03).

The project manager brings

- ☐ A laptop
- ☐ A USB-to-RS-485 adapter (to number a module or a probe, and to talk to one device alone)
- ☐ A loop calibrator (or a 4 to 20 mA source)
- ☐ A multimeter
- ☐ Screwdrivers (slotted and Phillips, small and medium)
- ☐ Wire strippers and a ferrule crimper
- ☐ A network cable tester
- ☐ Cable ties and labels
- ☐ A head torch
- ☐ Spare fuses and terminals
- ☐ A phone for photographs

You do not need a tool for work inside a live board: that is the electrician's. The spares kit (one for each project manager) goes in the car too.

Survey

About one hour, with the electrician if the plan needs one. Bring this pack, a phone for photographs, a tape measure, a torch and a notebook. No tools are needed to survey, and nothing is opened.

Ask, in this order

The answers decide what is measured and what it costs. Write them on the survey form that follows.

1. Who decides, and who gets called at night? Names, mobile numbers, emails: these become **Who is told**. Each alert message carries an *I have seen this* link, so nobody needs a login to acknowledge; the people who should also look at the screens get a login of their own, and a login needs an email address.
2. What went wrong in the last twelve months that cost money or a guest? Write it in their words. It is the reason they buy.
3. The last twelve electricity bills (price per kWh, kWh bought each month) and the water bills. The platform shows what solar kept on site at their price; without a price it shows kWh only.
4. Is there solar? What brand is the inverter, and where is its AC output? Is it allowed to send energy to the grid?
5. Where does the supply enter the building? Is it three-phase?
6. Where are the water tank, the pump and its starter? How tall is the tank? What is the pipe's pressure? Has the starter a spare "running" contact?
7. Is there a network socket in the plant room, or cellular signal? (Look at your phone there.)
8. Is there a power socket for the box, and is it on a circuit that stays on?
9. Who is the customer's electrician, and can they be there on install day?

Look at, and photograph

- The supply entry and the main board (closed): where a meter could be fitted with the clamps around the incoming phases.
- The inverter and its AC output cable.
- The tank, the pump, the starter, and any existing level or pressure gauge and flow meter.
- The place for the box: dry, 30 cm free, no heat, within reach of a socket and a network cable.
- The route for the data cable from the board to the box (under 100 metres; note any crossing of power cable).

CHECK

Go if there is a way to the internet (cable or cellular), a socket that stays on, a safe place for each meter, an electrician for the board work, and a person who answers when called.

No-go, politely, and write why, if the only place for a sensor is unsafe to reach, the customer wants something switched or controlled, or there is no responsible person to receive alerts.

☐ Go ☐ No-go, because: _____

Survey form

KIT H · HOTEL OR GUESTHOUSE

Field	Answer
Customer, site name and address, date	
Contact: name, mobile, email (first, second, third to be told)	
What went wrong last year (their words)	
Prices from the bills: electricity per kWh; paid for energy sent to the grid; water per m³	
Twelve electricity bills and the water bills collected	☐ Yes ☐ Later
Supply: single or three phase; main breaker size (A)	
Inverter: brand, size (kW), where its AC output cable is; allowed to send to the grid?	
Tank: height (m), water source; pump (kW); starter location; spare running contact on the starter; pipe pressure (bar)	
Meters needed: grid, solar (and where)	
Sensors needed: level, pressure, flow, pump running (and where)	
Network: customer's cable or cellular; router brand; who can give an address	
Power for the box: socket location	
Electrician: name, mobile, day	
Photographs taken (list)	
Go / no-go, and why	☐ Go ☐ No-go

The drawings

Every drawing is for kit H and says so. They show how the parts connect, not terminal numbers: follow the maker's manual for terminal numbers. Mains work is inside the dashed red box and is the electrician's.


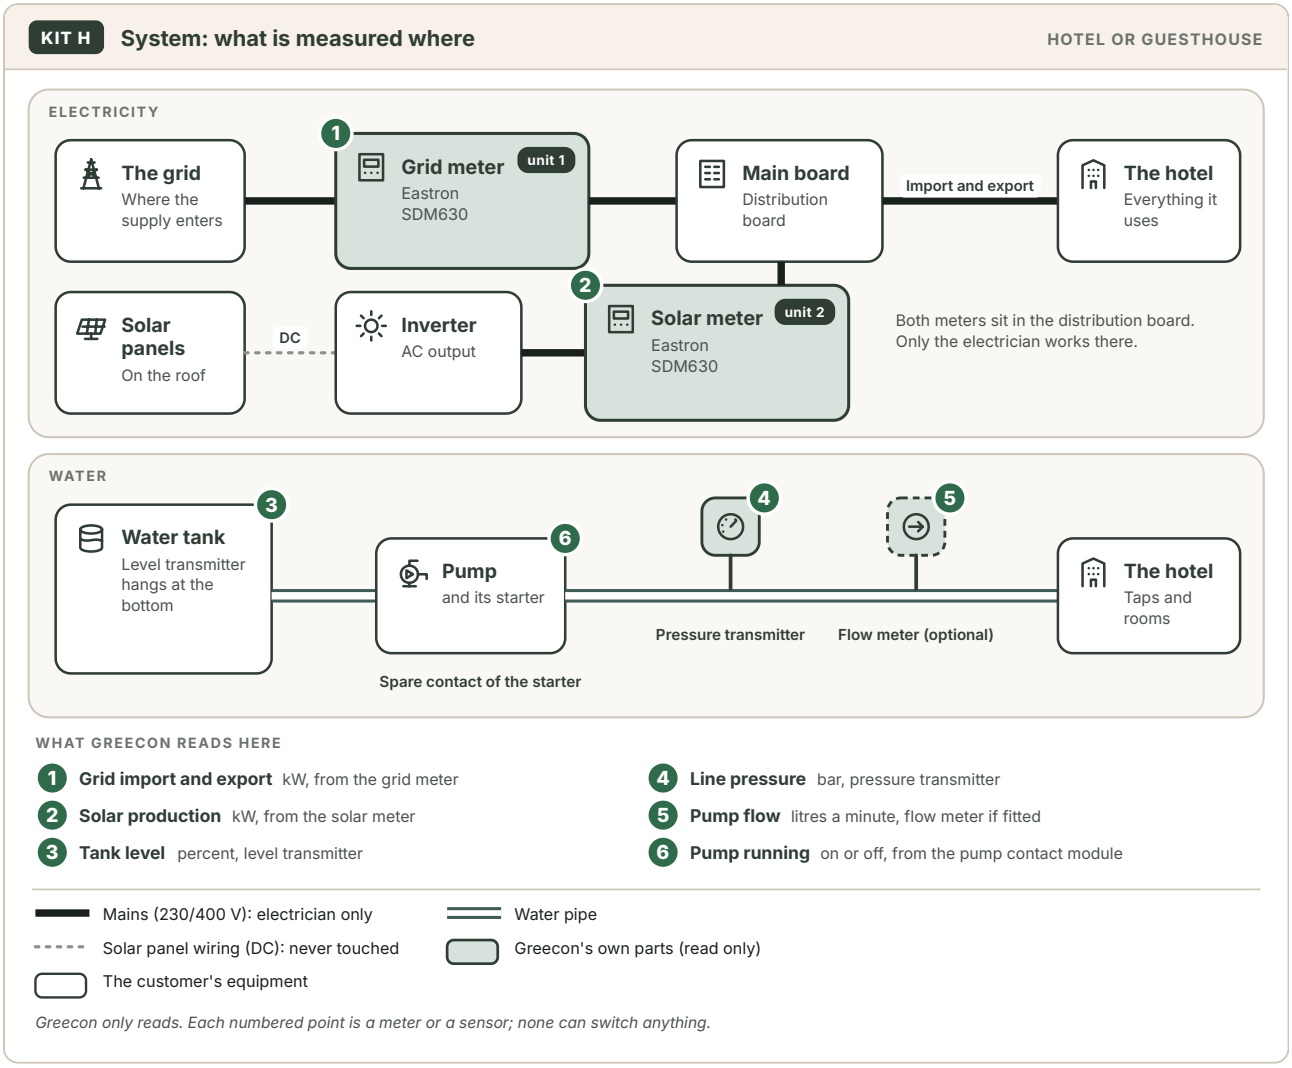



Figure H-1. Kit H, hotel or guesthouse. System: what is measured where. The numbers mark what Greecon reads; they are listed under the drawing.

KIT H **Wiring: the data cable, the signal wires and the mains side** BUS AND SIGNALS

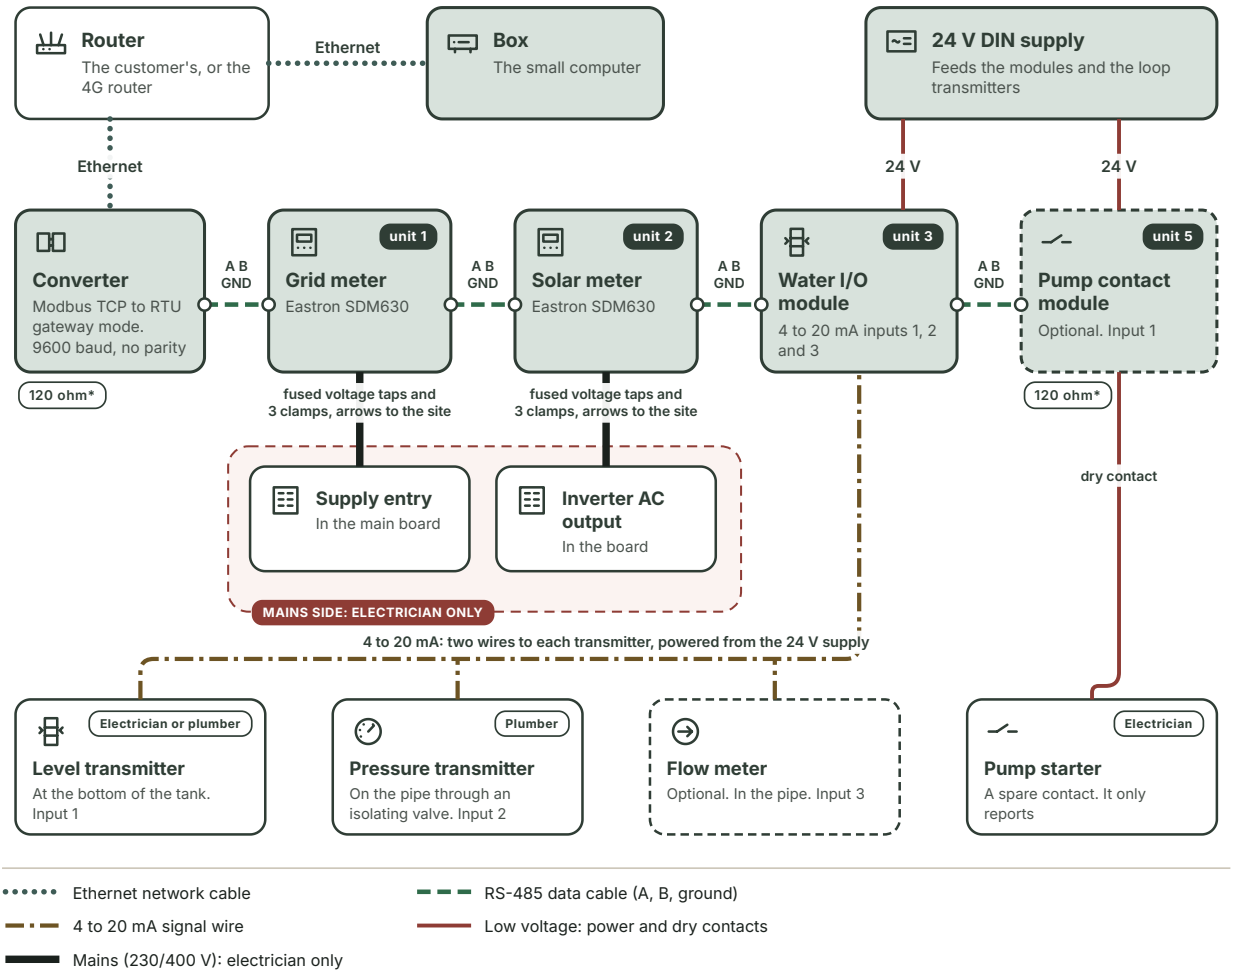


Only for runs longer than about 50 m, or if readings are unreliable at 9600 baud. The electrician wires the 4 to 20 mA loops and the contact. Terminal numbers are not drawn: follow the maker's manual for terminal numbers.

Figure H-2. Kit H. Wiring: one RS-485 cable from the converter through the grid meter, the solar meter and the water module to the pump contact module, with the 4 to 20 mA loops into the water module and the pump starter's contact into the pump contact module. Mains work is inside the dashed box.

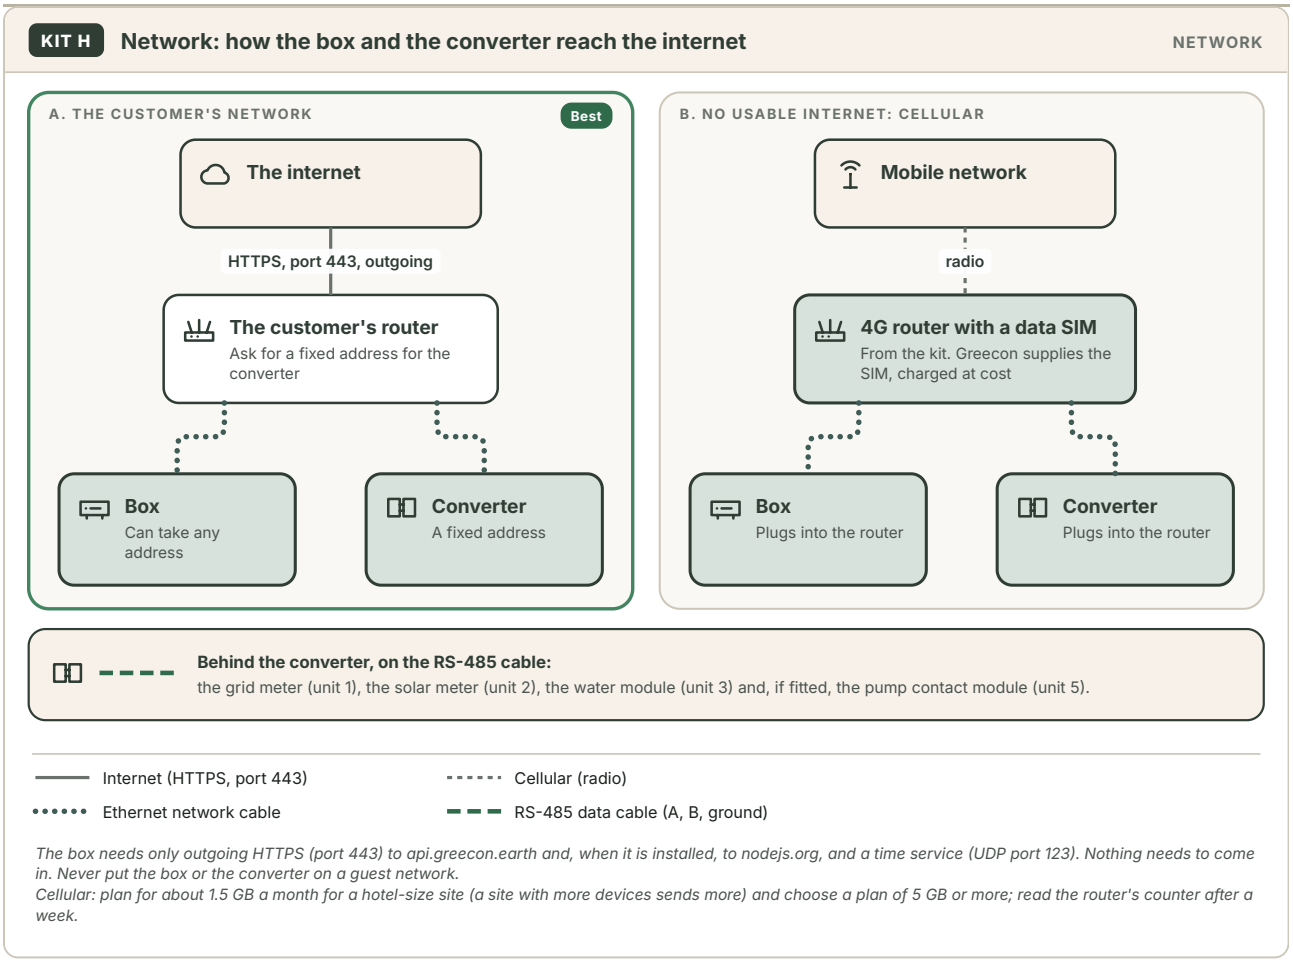

The box needs only outgoing HTTPS (port 443) to api.greecon.earth and, when it is installed, to nodejs.org, and a time service (UDP port 123). Nothing needs to come in. Never put the box or the converter on a guest network.
Cellular: plan for about 1.5 GB a month for a hotel-size site (a site with more devices sends more) and choose a plan of 5 GB or more; read the router's counter after a week.

Figure H-3. Kit H. Network: the box and the converter on the customer's router (best) or on a 4G router.

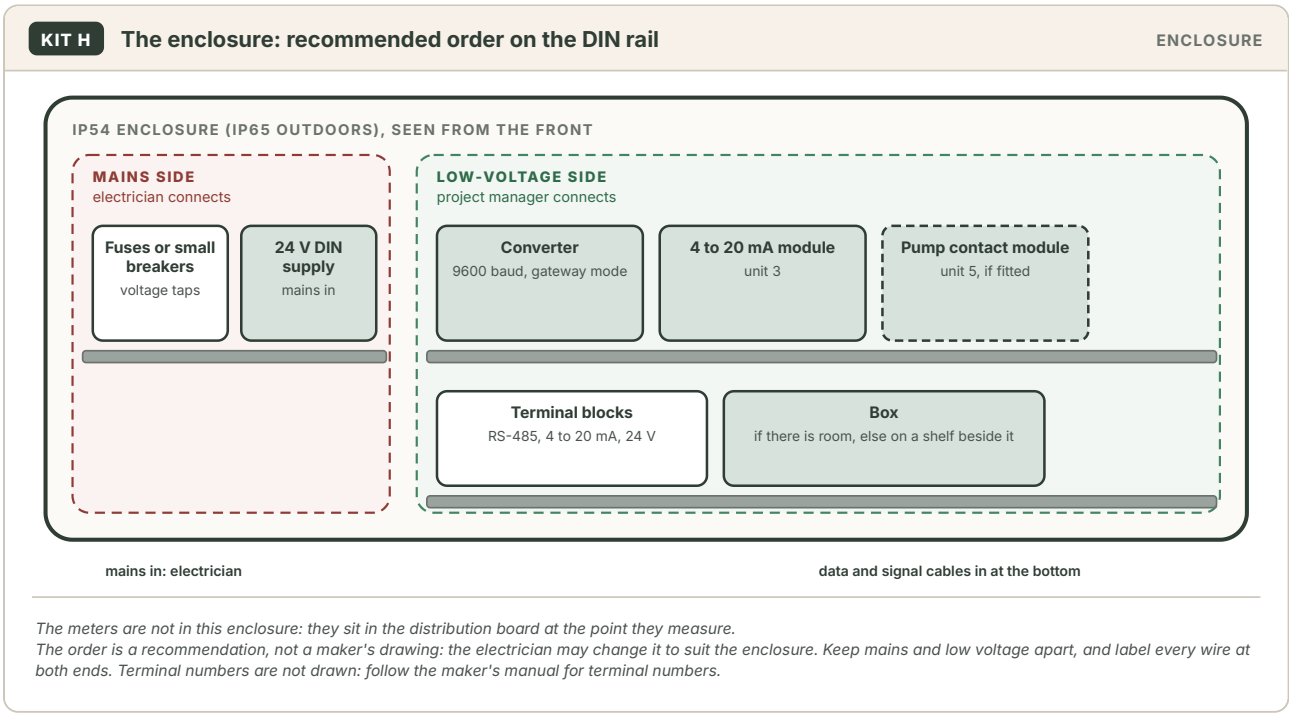

The meters are not in this enclosure: they sit in the distribution board at the point they measure.
The order is a recommendation, not a maker's drawing: the electrician may change it to suit the enclosure. Keep mains and low voltage apart, and label every wire at both ends. Terminal numbers are not drawn: follow the maker's manual for terminal numbers.

Figure H-4. Kit H. The enclosure: the recommended order of the parts on the DIN rail, mains side on the left.

The order on the rail is a recommendation, not a maker's drawing: the electrician may change it to suit the enclosure. Keep mains and low voltage apart, and label every wire at both ends.

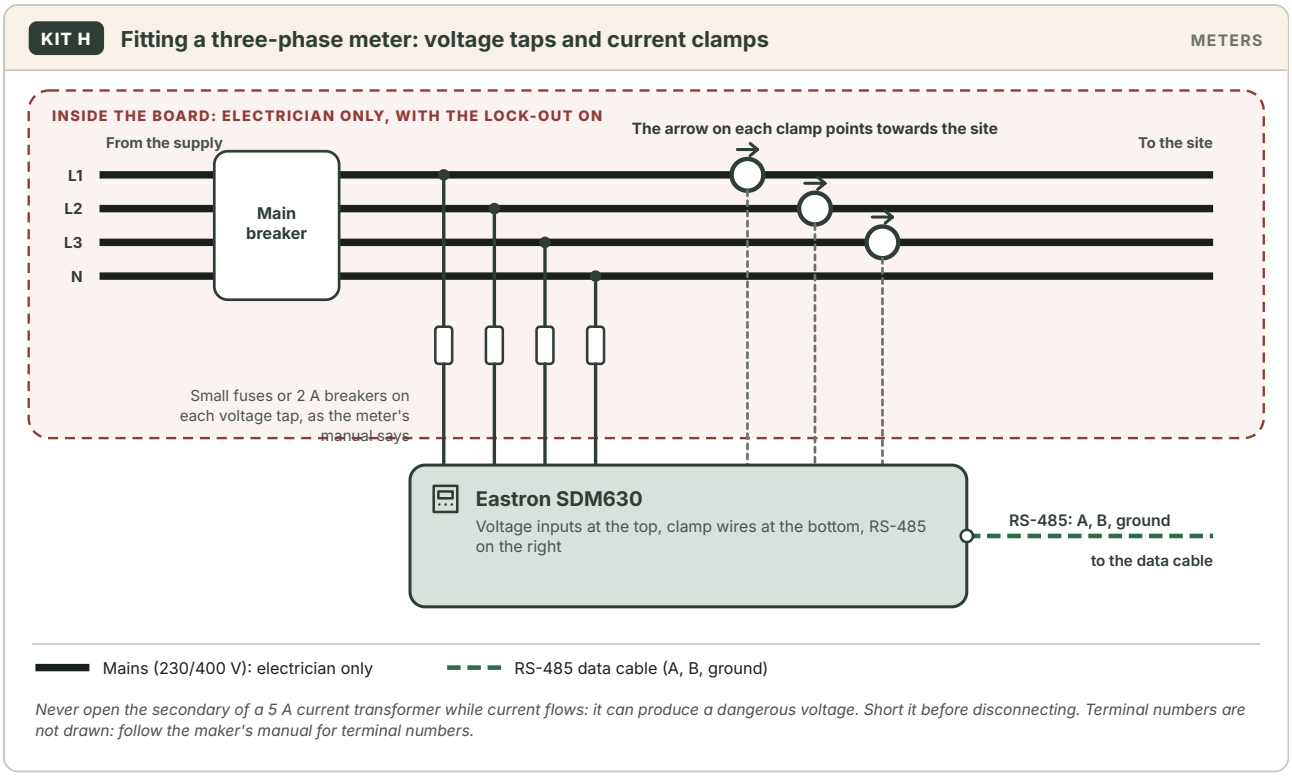


Figure H-5. Kit H. Fitting the grid meter and the solar meter: fused voltage taps and three clamps each, arrows towards the site.

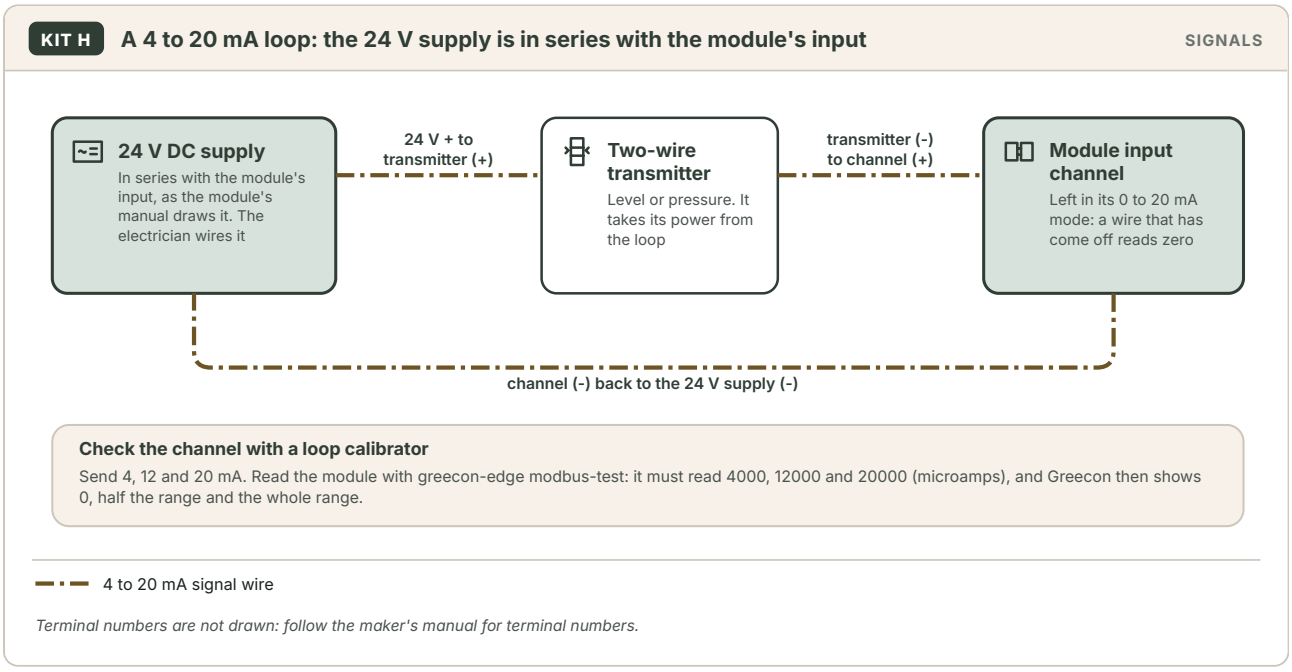


Figure H-6. Kit H. One 4 to 20 mA loop; the level, the pressure and the flow transmitter are each wired this way.

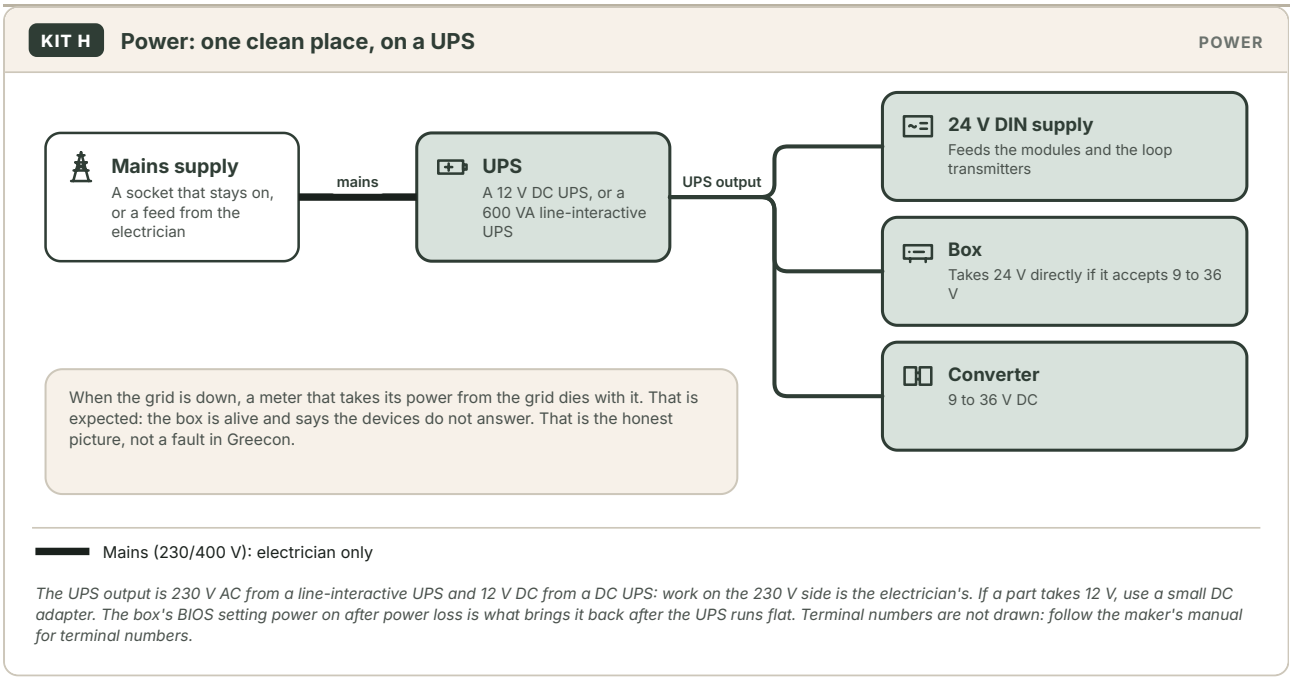


Figure H-7. Kit H. Power: the UPS feeds the box, the converter and the 24 V supply.

At the office

Everything in this chapter is done at the office, before the site visit, and it makes install day shorter. About 30 minutes in Greecon and about two hours for the box, and more for the first kit's numbers and its desk test: time it, and write it down. PROJECT MANAGER

In Greecon

- [ ] **Sign in** at `https://app.greecon.earth/login` with **Greecon team**. You land on **Today**.
- [ ] **A new customer:** if they asked through the web page, their request waits under **Requests waiting** on **Today** (and on **Requests**): press **Onboard**. Otherwise open **Clients** and press **Onboard a client** (top right): company name, owner's name, owner's email, then **Onboard client**. A box appears, **Client onboarded — save this password now**: it is the owner's temporary password, shown once. Write it on the handover page or tell it to the owner by phone. Do not send it by email. If a message says someone already has an account with that email, the person is already a customer: add the new site to the customer they already have.
- [ ] **Open the customer for setup:** in the customer's row on **Clients** press **Open for setup** (on **Today** the same button is **Open account** for a site that needs a look and **Continue setup** for a site being set up). You land on the customer's **Sites** page, with a banner saying you are there as Greecon staff, setting it up. Everything you do is recorded under your own name. The setup session lasts four hours: after that, sign in again with **Greecon team** and press **Open for setup** again. What you saved is still there.
- [ ] **Make the site:** on **Sites** press **Add a site**. In the form (*New site from a template*) choose **What kind of site**: **Hotel or guesthouse**. The page lists what the template will contain. Enter **Site name** and **Where it is**, check **Currency of the bills** (it starts as ALL) and **The site's own clock** (Europe/Tirane), and press **Create the site and start setting it up**.

- [ ] **Write down that the papers are signed:** you land on the setup page, titled **Set up** and the site's name, which says `0 of N steps done`, and its first step is **Order form signed and data terms agreed**. With the signed order form and the agreed data terms in front of you, write in the box who signed for the customer and on what date (it cannot be left empty), and press **The papers are signed**. Nothing goes into a customer's building without both papers.

- [ ] **Print the install card:** the link **The install card** is at the top of the setup page. It is your list for the visit: what to bring, what each device is set to and its number, how it is wired, the converter's settings, and what the customer's network is asked for. At the bottom are three messages to copy: send the first to the customer's contact two or three days before, and the second to whoever looks after their network. Each is in English with an *Albanian draft* folded under it, and someone who writes Albanian every day reads the draft before it is sent.

- [ ] **Get the install line:** on the same page press **Add the box and get its install command**. A line appears, beginning `curl -fsSL https://api...` and ending in a code like `GRC-XXXX-XXXX-XXXX`. Copy it with the copy button. It is shown once. The code works once, for seven days. Press **I have copied it**.

> **STOP**
>
> **The install line is the box's key.** Anyone with the line can install a box as this site until it is used or has expired. Treat it like a password: not in email or chat, and pasted straight into the box. If it is lost, or the seven days have passed, press **Install a box, or replace this one** on the same step; it asks you to confirm and shows a new line. The old line then stops working, and the box that uses the new line takes the place of the box now installed.

The box on your desk

The operating system and the pasted install line are still a terminal job; everything after them is done on the setup page.

- [ ] **Install the operating system** on the box: Debian 12, Ubuntu 22.04 or later, or Raspberry Pi OS 64-bit, with the SSH server on, one user with a long password, and the time zone set to Europe/Tirane. The twenty-minute recipe and the BIOS settings are in the Hardware Reference (PDF 03), section 4.3.

- [ ] **Connect the box** to your office network and open a terminal on it (a keyboard and screen, or SSH).

- [ ] **Paste the install line exactly.** It runs in seven numbered steps and tells you each one: checking the box (and that it can reach Greecon and agrees with it about the time), installing Node.js, making the places the software uses, fetching and checking the Greecon software, giving the box its own credential, starting the service, and waiting to hear that Greecon can see the box. It finishes with `Done. Greecon can see this box.`

- [ ] **Refresh the setup page. Install the box** now says **Done**, with the box's name, its version and "Heard from N seconds ago". You did not press anything to make it so: the platform saw the box.

- [ ] **Label the box** with the site name and the date, and pack it. The box keeps its credential when it is moved: unplug it, carry it to the site, plug it in, and it reports from the new place without anything being typed again.

- [ ] **Pack the rest** of the kit from the shopping list, the tools, the spares kit, the printed pack and the printed install card.

The numbers and the converter

The kit is made of approved models, and every device has the same number on the cable in every kit. You set them here, at the office; on site you only check the labels and do not change them. The numbers for this kit are in the table under **Numbers, addresses and ranges** and on the install card. Everything on one cable is

9600 baud, 8 data bits, no parity, 1 stop bit.

- [ ] **Set each meter's number on its own display,** one meter at a time (delivered as unit 1, two on one cable would answer over each other). The SDM630 is delivered at 9600 baud: check it. The SDM230 is delivered at a speed that depends on its version (the V1.6 manual says 2400): set it to 9600, on the Baud Rate page. Powering a meter on a bench is mains work: the electrician makes up the office's bench lead, and you never wire mains.
- [ ] **Number the two Waveshare modules** with the maker's setting tool and a USB-to-RS-485 adapter, one at a time (each is delivered as address 1, and there is no switch): **3** on the 4 to 20 mA module (Modbus RTU Analog Input 8CH) and **5** on the pump contact module (Modbus RTU IO 8CH). Use the version of the 4 to 20 mA module that reads current, not the one that reads voltage, and leave its inputs in their default 0 to 20 mA mode, on purpose: a 4 to 20 mA transmitter then reads 4000 to 20000 microamps, and a wire that has come off reads 0, below the 4 mA of an empty tank, which Greecon can see and say.
- [ ] **Set the converter** in its web page: mode **Modbus TCP to RTU (gateway)** (not transparent, not raw TCP, not Modbus RTU over TCP), 9600 baud, 8 data bits, no parity, 1 stop bit, TCP port 502. Its address on the customer's network is arranged on site: a fixed one is best, and Greecon finds the converter either way.
- [ ] **Label every device with its number** and the converter with its settings, and photograph the labels.
- [ ] **Test the kit on the desk.** The registers of the two Waveshare modules are from the maker's published tables and have not been tried on real hardware, so the first real kit is rehearsed on a desk before it is trusted (the Project Manager Field Manual (PDF 02), section 3.11). Anything that differs from this book is reported to Greecon.



If the line stops with `STOP:` it says what to check and how. If it stopped before step 5, *Giving this box its credential*, fix the cause and run the same line again: the code has not been used yet. From step 5 on, the code is used up, and the same line would stop with "Greecon did not give the software to this box". Then run the line again with no code at the end: `curl -fsSL https://api.greecon.earth/edge/install.sh | sudo bash -s --`. That repairs the box and keeps its credential. If it answers "This box has no code and has not been installed before", the box never got its credential: press **Install a box, or replace this one** and use the new line. The commonest stops are a box that cannot reach Greecon (no internet, a firewall that blocks outgoing HTTPS on port 443, or a clock so far out that secure connections fail), and a code already used or older than seven days. A clock only minutes out does not stop the install: it prints a warning, and the setup page later says its clock is N minutes fast.



The first time, rehearse the whole job on a desk with a laptop standing in for the kit: the Project Manager Field Manual (PDF 02), section 3.11. It takes an afternoon and finds the mistakes in the room instead of at the customer's.

Install day

About four to six hours. The electrician and the project manager work at the same time, in this order, so that nobody waits. The left edge of each row is black for the electrician, green for the project manager and sand for the customer.

	#	Who	Do this
☐	1	ELECTRICIAN, PROJECT MANAGER	**Before anyone touches anything:** the signed papers are in your hand, the electrician is there, and the lock-out is agreed. **Walk the site together.** Agree where each meter and sensor goes. Photograph everything before you start.
☐	2	CUSTOMER	Show the way to the main board, the inverter, the tank room and the starter. Have the router and a socket that stays on ready, and the person who can give the converter a fixed address.
☐	3	ELECTRICIAN	**Apply the customer's lock-out** on the board to be worked on.
☐	4	ELECTRICIAN	**Fit the grid meter** at the supply entry: voltage taps with their small fuses or 2 A breakers as the meter's manual says, and the three current clamps around the incoming phases, **arrow towards the site**. Figure H-5.
☐	5	ELECTRICIAN	**Fit the solar meter** on the inverter's AC output, after the inverter and before the distribution board: the same, clamps with the arrow towards the site.
☐	6	ELECTRICIAN	**Connect the pump's run contact** (a spare auxiliary contact of the starter, as a dry contact) to **input 1 of the pump contact module**, as the module's manual draws it (its DI COM left unconnected). Never to a control circuit, and never to the module's relay outputs: the contact only reports. If the starter has no spare contact there is no module: it is taken off the list in setup step 4.
☐	7	ELECTRICIAN, PROJECT MANAGER	**Fit the level and pressure transmitters** (and the flow meter, if there is one) with the customer's plumber for the wet parts, and **wire their 4 to 20 mA loops** with the 24 V supply in series, as the module's manual draws it: **level on input 1, pressure on input 2, flow meter on input 3.** The level transmitter hangs at the bottom of the tank and must be rated for drinking water. The pressure transmitter goes on the pipe through an isolating valve. Figure H-6. You check each is on its own input and number the wires at both ends.
☐	8	PROJECT MANAGER	**Mount the enclosure** and in it the converter, the two modules (4 to 20 mA and pump contact), the 24 V supply and the UPS (the box too, if there is room, otherwise on a shelf beside it). Figure H-4.
☐	9	PROJECT MANAGER	**Run the RS-485 data cable** from the converter to the grid meter, on to the solar meter, then to the 4 to 20 mA module and the pump contact module: one cable, a daisy chain, no branches. Shielded twisted pair, the shield joined to ground at one end only, away from power cables. The electrician connects its ends at the meters' A and B terminals inside the board. Figure H-2.
☐	10	PROJECT MANAGER	**Check the labels:** the number on each device against the table under *Numbers, addresses and ranges* (grid meter 1, solar meter 2, water module 3, pump contact module 5). They were set at the office: do not change them. Photograph each label.

	#	Who	Do this
☐	11	PROJECT MANAGER	**Check the converter's label** (gateway mode, 9600 baud, 8 data bits, no parity, 1 stop bit, port 502) and **connect the network:** plug the box and the converter into the customer's router, or into the sockets of the 4G router if the site has no usable internet. Ask for a fixed address for the converter and write it down. Figure H-3.
☐	12	ELECTRICIAN PROJECT MANAGER	**Photograph before closing:** every meter's label (model and serial number), the wiring, the converter's settings. Then close the board.
☐	13	ELECTRICIAN	**Remove the lock-out** only when you both agree the work is closed up.
☐	14	PROJECT MANAGER	**Power up** the UPS, the 24 V supply, the converter and the box.
☐	15	ELECTRICIAN	**Stay until commissioning is done.**
☐	16	PROJECT MANAGER	**Open the customer for setup again** on your laptop (the four hours are over by now) and go down the platform's setup list: **Find equipment**, the ranges, and the electrician's name and licence number.

Numbers, addresses and ranges

The numbers on the cable were set at the office. The box finds where the converter is. You give the range printed on each transmitter's label. You type no IP address, no port and no register.

The numbers on the cable

All four devices are behind one converter: they share its address and port 502, and differ only by number. Check each label against this table on install day. **Do not change a number on site.**

Device in Greecon	Make and model	Number	Label checked	Address found (the converter's)
Grid meter	Eastron SDM630	1	☐	
Solar meter	Eastron SDM630	2	☐	
Water I/O module	Waveshare Modbus RTU Analog Input 8CH	3	☐	
Pump contact module (optional)	Waveshare Modbus RTU IO 8CH	5	☐	

The Eastron meters and the pump contact module

Nothing to type: the template fills in their registers. For the meters it is total active power, input register 52 (a manual's 30053; counted from zero), a 32-bit floating point number with the high half first, in watts, multiplied by 0.001 to make kW; for the pump contact module it is digital input 1. Check the module by eye: with the pump running, **Pump running** reads 1; stopped, 0. Test from the box:

```
greecon-edge modbus-test --host 192.168.1.50 --unit 1 --type input --address 52 --data-type
float32
greecon-edge modbus-test --host 192.168.1.50 --unit 5 --type discrete --address 0
```

The ranges on the labels

One form for each transmitter (step 5 of the setup list), in the label's own words. Read the range from the label on the transmitter and measure how tall the tank is inside, from the bottom to the top of the water when it is full.

Reading	Input	The form asks for	Range on the label	Tank height
Tank level	1	Level transmitter: the range on the label (m or bar) and how tall the tank is inside (m)		
Line pressure	2	Pressure transmitter: the top of the range (bar)		
Pump flow	3	Flow meter: the top of the range (lpm, litres a minute)		

Greecon works out the register and the scale: 4 mA is 0 and 20 mA is the range (for the tank, range ÷ tank height × 100: a 0 to 5 m transmitter in a tank 4 m tall gives 125, and a full tank, at 16.8 mA, reads 100). **A transmitter shorter than the tank is refused:** it cannot see the top of the water. **No flow meter?** Tick **Not fitted at this site** under Flow meter: its reading is taken away, and the handover says that the no-flow alert cannot be raised. **No spare contact for the pump?** Press **The site does not have this: remove it** under the pump contact module in step 4.

The platform's setup list

The platform keeps its own list for each site. Open the site's setup page (**Set up** and the site's name). It shows up to twelve steps, always in this order; a step that does not apply to the site is left out. Each step is **Done**, **To do**, **Waiting** for another step, or **Needs attention**, and the banner at the top, **Do next**, names the step to do next. The platform works most steps out by itself: you press buttons only for what a person must check or say. Near the top are links to the site page, to **The install card** (the card for the visit) and to the **Handover sheet**.

	Step	Title on the setup list	Done by
☐	1	**Order form signed and data terms agreed**	Project manager
☐	2	**Prices from the customer's bills**	Project manager (optional)
☐	3	**Install the box**	Project manager
☐	4	**Where each device is on the network**	Project manager
☐	5	**Which register holds which reading**	Project manager
☐	6	**Every device answers the box**	The platform, by itself
☐	7	**Readings arrive and look right**	The platform, by itself

	Step	Title on the setup list	Done by
☐	8	**Someone is told when the site needs attention**	Project manager
☐	9	**Grid meter direction checked**	Project manager, with the electrician
☐	10	**Alert limits agreed with the customer**	Project manager
☐	11	**Electrical work done by a licensed electrician**	Project manager, with the electrician
☐	12	**Commissioned**	Project manager

Below, each step says what to do, what you should see, and what to do if you do not.

Step 1 Order form signed and data terms agreed

PROJECT MANAGER

DO	Nothing goes into a customer's building until the order form is signed and the data terms are agreed. Greecon keeps the papers; the platform cannot see a signature, so you write down that they exist. In the box above the button write **who signed for the customer and on what date** (for example *Signed for the hotel by Besa Krasniqi on 19 October*): it cannot be left empty. Press **The papers are signed**. Do this at the office, and bring copies on install day.
YOU SHOULD SEE	The step turns **Done**: *Signed and agreed.*, with your name, the time and what you wrote. They are on the handover sheet.
IF YOU DO NOT	Until it is done, commissioning stays grey. The button will not work while the box is empty. If a paper turns out to be wrong, press **Reopen** (if the site had been commissioned, that is taken back too).

Step 2 Prices from the customer's bills

PROJECT MANAGER *optional*

DO	Open **Enter prices and baseline** (once something is entered it is called *Prices and baseline*; the same form is on the site's page). Enter the currency; the electricity price per kWh from the latest bill; what is paid for energy sent to the grid (leave it blank if nothing is paid); the water price per m³; a typical month before (the kWh bought and the m³ of water, from last year's bills); where those numbers came from; whether the site cannot send energy to the grid (tick it if the plant is zero-export); and the time zone, `Europe/Tirane`. Press **Save**.
YOU SHOULD SEE	The step turns **Done** and lists the prices, for example *Electricity: N ALL per kWh* (and *Water: N ALL per m³* where the site has a water flow reading).
IF YOU DO NOT	It stays **To do** and says *Not set: Greecon shows kWh but cannot say what they are worth.* That is allowed: this step is optional and does not hold up commissioning, and without a price Greecon shows kWh only. Without the typical month before, no comparison is shown, which is correct.

Step 3 Install the box

PROJECT MANAGER

DO	Press **Add the box and get its install command** and copy the line it shows (shown once, works once, lasts seven days). Run it on the box exactly as shown. This is done at the office, before install day.
YOU SHOULD SEE	**Done**, with the box's name, its version and *Heard from N seconds ago.* You do not press anything to make it so: the platform saw the box.
IF YOU DO NOT	▪ *Waiting for the install command to be run on the box.* The line has not been run yet. ▪ *The box has its credential but has not reported yet.* Wait a minute and check the network cable. ▪ *Last heard from N ago: it is offline.* Check the box's power, the network cable and the site's internet. On the box: `greecon-edge status` and `journalctl -u greecon-edge -n 50 --no-pager`. ▪ *Online, but its clock is N minutes fast* (or slow). Run `sudo timedatectl set-ntp true`.

Step 4 Where each device is on the network

PROJECT MANAGER

DO	Press **Find equipment**. Nobody types an IP address, a port or a unit number here. - The box looks at the site's own network (local private addresses only, port 502, about a minute) and only reads. The page says *The box is looking at the network now.* and updates by itself. The platform recognises what answered and fills in at once only what is certain: a device with no address, found at the kit's own number. The rest waits for you. - A device **Found** but not filled in (another address, another number, another meter model): read the line and, if it makes sense, press **Use this address** (or *Use these N addresses*). An optional device the site does not have: press **The site does not have this: remove it**. - The soil probe, the weather sensor and a battery are entered by hand: under the device open **Enter the address by hand** (soil probe 6, weather sensor 7). - Box not on your network (a desk rehearsal), or a converter on another port: open **I know the converter's address**, type its address (and its port, if not 502), and press **Look at this address**.
YOU SHOULD SEE	Each device gets a line in plain words: **Set** (found, address filled in), **Found**, **Not found**, **Not sure which** or **Enter by hand**. When it worked the step is **Done** (*Every device has an address.*), and the button reads **Look again**.
IF YOU DO NOT	- **Not found**: *Nothing that looks like an Eastron meter answers at unit 2. Check the address set on it, the speed, and the A and B wires.* An optional device the site does not have: press **The site does not have this: remove it**. - **Not sure which**: Greecon will not guess, because a wrong guess could swap the grid meter and the solar meter. Read each device's label, use **Enter the address by hand** under each with the number on its label, then **Look again**. Numbers are set at the office: a part with a wrong number goes back there. - *No Modbus converter answered on this network:* check that the converter is on and plugged into the same router as the box. *A converter answers at 192.168.1.50, but nothing answers behind it:* check each meter's address, the speed and the A and B wires. *All answered with exactly the same words:* the converter is not in gateway mode. *The box did not pick this up:* check that it shows as online in the step above. - Readings that stop after it had worked: the router may have given the converter a new address. Press **Find equipment**, then **Use this address**.

Step 5 Which register holds which reading

PROJECT MANAGER

DO	The Eastron meters and the pump contact module need nothing typed. For the 4 to 20 mA module the page asks, for each transmitter, only for the range printed on its label, in the label's own words: - **Level transmitter** (input 1): the **Range on the label**, for example 5, its **Unit on the label** (metres, or bar) and **How tall the tank is inside** in metres, for example 4: from the bottom to the top of the water when full. - **Pressure transmitter** (input 2): the **Top of the range** in bar; 10 is usual. - **Flow meter** (input 3): the **Top of the range** in litres a minute. Greecon works out the register and the scale. For a transmitter the site does not have (no flow meter), tick **Not fitted at this site**: Greecon asks first, then takes the reading and its history away. Press **Save the ranges**. Equipment Greecon does not know (the soil probe, the weather sensor, a battery) is mapped by hand, from the maker's register table: under the reading press **Choose the register** and fill in the register kind (**Input** for a manual's 3xxxx, **Holding** for 4xxxx), the address (counted from zero: 30053 is address 52, 40001 is address 0), the kind of number (and which half comes first), how it becomes the reading (**Multiply and add**, or **A straight line, such as 4-20 mA**) and which part of the value. Press **Save the register**.
YOU SHOULD SEE	**Done**: *Every reading is tied to a register.* Under each transmitter the form says what it set, for example *Set now: 4 mA is 0 % and 20 mA is 125 %.* (0 to 5 m in a tank 4 m tall); the tank level is a percentage of the tank, so a full tank reads 100.
IF YOU DO NOT	*N readings not tied to a register yet*, each marked *Needs the range printed on the transmitter's label.* (the 4 to 20 mA module) or *No register chosen.* (equipment Greecon does not know). A transmitter shorter than the tank is refused: *The transmitter reads up to 3 m and the tank is 4 m tall: it cannot see the top of the water. Fit a transmitter with a longer range.* A reading the site does not have holds the list here: tick **Not fitted at this site**, or press **The site does not have this: remove it** (step 4) for an optional device.

Step 6 Every device answers the box

THE PLATFORM

DO	Nothing to press: the platform does this one by itself once the box is online and each device has its address and registers. Wait a minute.
YOU SHOULD SEE	Each device shows **Done**: *Answering (N readings)*. On the box, `greecon-edge status` lists each device as **ok**.
IF YOU DO NOT	The device shows **Needs attention** with the reason in words, for example *no answer from 192.168.1.50:502 (unit 2)*. Look in this order: the converter's address may have changed (press **Find equipment** again, then **Use this address**); the number on the device's label against the install card; the speed at the converter; A and B swapped on the data cable; the converter not in gateway mode. Nothing answers at all: the converter is off, or it is on another network than the box. Test one register from the box with `greecon-edge modbus-test` (see the box commands): if it prints *Could not read*, the problem is the wiring or the settings, not Greecon.

Step 7 Readings arrive and look right

THE PLATFORM

DO	Nothing to press. Look at each reading: is it a number you believe?
YOU SHOULD SEE	Each reading shows **Done** with its value and age, for example *N %, 4 seconds ago*, and the step says *Every reading is arriving and could be real.* **Pump running** reads 1 while the pump runs and 0 while it is stopped.
IF YOU DO NOT	*No reading yet*: wait a minute. *Last reading N ago. It has stopped arriving*: a device or the converter lost power, or a cable came loose. A value that cannot be real says so, for example *-31.2 cannot be a tank level (0 to 100). Check the register address, the scale or the sensor.* On a transmitter a reading below zero is nearly always a wire that has come off (the module then reads 0, below the 4 mA of an empty tank); one far too high is a range or tank height typed wrongly: give the ranges again (step 5).

Step 8 Someone is told when the site needs attention

PROJECT MANAGER

DO	Open **Who is told**. **Add a person** for each name from the survey, in the order they should be told (each needs an email, a mobile number with its country code such as `+355 69 123 4567`, or both; give everyone an email address as well as a number). Press **Save the list**. Press **Send a test message** beside each person and ask them whether it arrived: in the inbox, not in spam; on the phone. Tell each person that every alert message has an *I have seen this* link: one tap, no sign-in, and it stops the message going on to the next person. Give a login of their own (the Operator role) only to those who should also look at the screens. Then, back on the setup list, press **I checked this**.
YOU SHOULD SEE	After the test: *A test message was sent N ago. Greecon cannot tell whether it was read.* After you press the button: **Done**, *A test message reached the person on the list.* The button stays grey until the list has someone on it and a test has been sent.
IF YOU DO NOT	▪ *This Greecon platform is not set up to send messages:* tell the founder; the email service must be switched on before a site can be commissioned. ▪ *Nobody is set to be told:* add the people. ▪ *Nobody on the list has an email address* (or a phone number): add one for each person. ▪ A message that did not arrive: look at **What was sent** under **Who is told**, check the address and the country code, and ask about spam. ▪ *Test messages are limited to 6 an hour.* Wait and try again.

Step 9 Grid meter direction checked

PROJECT MANAGER | ELECTRICIAN

DO	Greecon cannot see which way the meter's clamps point. With the sun down or the solar switched off, switch on a known load (a kettle or a heater). **Grid import must go up.** If **Grid export** goes up instead, the clamps are the wrong way round: the electrician turns them (with the lock-out on) and you check again. Then press **I checked this** with a note of what you saw.
YOU SHOULD SEE	Before: **To do**, *Greecon cannot see which way the meter's clamps point.* After you confirm: **Done**, *Checked on site,* with your name and the time.
IF YOU DO NOT	Import and export swapped: the clamps are the wrong way round. The electrician turns them; you repeat the check. A reversed clamp swaps what the site buys with what it sells, and every figure with it.

Step 10 Alert limits agreed with the customer

PROJECT MANAGER

DO	The step lists each reading that has limits, with what applies. Go through them with the customer and agree numbers they would act on. To change one, open the **Standard** drop-down beside the reading (it says *1 set*, *2 set* once changed), type the numbers and press **Save limits**. When they are agreed, press **I checked this**.
YOU SHOULD SEE	Each reading with limits is listed with its numbers, for example *Tank level: Critical below 15 % (standard); Low below 35 % (standard).* After you confirm: **Done**, *Checked on site.*
IF YOU DO NOT	The standard limits apply until you change them: tank **Critical below 15 percent** (an Act now alert) and **Low below 35 percent** (a Check today alert); pump **No flow at or below 0.2 litres a minute** (an Act now alert once it has held for 30 seconds, raised only when the box reads both a flow and the pump's running state); battery **Low below 25 percent**. **Start irrigating below** has no standard value: Greecon gives no irrigation advice until the grower's own value is entered.

Step 11 Electrical work done by a licensed electrician

PROJECT MANAGER | ELECTRICIAN

DO	Fitting meters in a board and wiring transmitters and contacts is the **licensed electrician's** work, under the customer's lock-out. When the electrician has finished and the lock-out is removed, ask for their name and licence number, photograph the wiring, the labels and the displays, and check that the lock-out has been removed. Then write in the box the electrician's **name and licence number** (for example *Arben Hoxha, licence E-1234*), or that no electrical work was needed: it cannot be left empty. Press **The electrical work is done**.
YOU SHOULD SEE	The step turns **Done**: *Done by a licensed electrician.*, with your name, the time and what you wrote (they are on the handover sheet). The platform does not check the licence: what you write is the record.
IF YOU DO NOT	Until it is done, commissioning stays grey. Do not press the button while the work is open or the lock-out is still on. The button will not work while the box is empty.

Step 12 Commissioned

PROJECT MANAGER

DO	Greyed out until every other step is done (optional steps do not hold it). Then it says: *On site, compare what Greecon shows with what you can see: the meter's own display, the tank, the pressure gauge. When they agree, confirm here.* Do the commissioning tests in this pack, write the pairs of numbers on the record, then press **Commission this site** with a note.
YOU SHOULD SEE	The progress line reads **Commissioned.**, your name and the date are on the handover sheet, and **Open the handover sheet** appears.
IF YOU DO NOT	While it is grey it says *N steps above must be done first.* and *Finish the steps above.* Finish them first.

Commissioning

Commissioning is checking, once, on site, that what Greecon shows is what the real world is. PROJECT MANAGER with the electrician and the owner's own person.

- Compare in the order of the table, and write the pair of numbers (what Greecon shows, what you can see) on the record.
- **Do not start, stop or open any equipment yourself.** The owner's own person does, because they know what else it affects.
- A check that fails is not commissioned: find the cause (the three most likely problems are at the end of this pack), fix it and check again. When every line passes, press **Commission this site** on the setup list (step 12) with a note. It stays grey until every other step is done, the papers (step 1) and the electrician's name and licence number (step 11) included. The progress line then reads **Commissioned.**, and your name and the date are on the handover sheet.

DO

The internet cut, step by step. Cut only the site's internet, for ten minutes: unplug the router's uplink cable (the one that goes to the wall or the modem), or take the SIM out of the cellular router. **Leave the box and the converter plugged into the router:** if the box cannot reach the converter it reads nothing, and there is nothing to test. While it is out, `greecon-edge status` shows a queue. Then restore the internet. A few minutes after it returns the queue is empty and the readings from the gap are in the downloads. **Write the result down:** it is the evidence for the statement that the box keeps its readings.

Check and how	Pass when	Greecon shows	Real	Result
Grid meter's display against Greecon. Read the display (kW or W) and Greecon at the same time.	Within 5 percent, or 1 kW on a small load			☐ Pass ☐ Fail
Solar meter's display against Greecon. The same, on the solar meter.	Within 5 percent, or 1 kW on a small load			☐ Pass ☐ Fail
Grid direction. A known load on (a kettle or a heater), the sun down or the solar off.	Import rises; export does not			☐ Pass ☐ Fail
Solar at night.	Zero, or a few watts			☐ Pass ☐ Fail
Solar at midday. Against the inverter's own display.	Within about 5 percent			☐ Pass ☐ Fail
Tank level. A dipstick or the sight gauge, at two levels.	Within 5 percentage points			☐ Pass ☐ Fail
Pressure. Against the pressure gauge on the same line.	Within 0.2 bar			☐ Pass ☐ Fail
Flow (if there is a flow meter). A bucket test (fill a measured volume, time it), or the flow meter's own display.	Within 10 percent			☐ Pass ☐ Fail

Check and how	Pass when	Greecon shows	Real	Result
Pump running. The owner starts the pump.	Greecon shows running within 30 seconds, and changes both ways			☐ Pass ☐ Fail
4 to 20 mA channels. With a loop calibrator, send 4, 12 and 20 mA.	The reading at the bottom, the middle and the top			☐ Pass ☐ Fail
A test message. Each person on the list.	It arrived, in the inbox and on the phone			☐ Pass ☐ Fail
Power cut. Unplug the box for 30 seconds, plug it in.	Back reporting within 3 minutes, and the box says nothing about readings lost			☐ Pass ☐ Fail
Internet cut (the first install, and any time the box or its software is new). See the box above.	A queue while it is out; empty a few minutes after it returns			☐ Pass ☐ Fail

Signed off by: _____ Date: _____

Handover

About 30 minutes at the customer's, with the owner and the owner's people who are told. PROJECT MANAGER

- ☐ **Print the handover sheet.** On the setup page open **Open the handover sheet**, check it, and print it (**Print or save as PDF**; the printed page leaves out the menus). It names the customer and the site, says where each device is (address, unit number, registers), who is told, what was commissioned and by whom, who signed the papers and who the electrician was, and how to reach Greecon (`info@greecon.earth`).
- ☐ **Show the owner, in ten minutes, in this order:** the **Overview** (is everything all right, in one sentence); **Energy now**, the flow moving from the solar to the site and the grid; **Value**, what the solar kept on site this month and the prices it uses; the site's own page under **Sites**, with the tank level, the pressure and whether the pump runs; **Who is told** (under **Settings**) and a live test message arriving on their phone, and that each message carries an *I have seen this* link, so that nobody needs a login to acknowledge an alert; **Reports**, under **Downloads**.
- ☐ **Say the two things in the boxes below, in these words:** what Greecon is, and how an alert reaches people.
- ☐ **Leave** the printed sheet, signed; the box's label; and a card with `info@greecon.earth` and your phone. **File** the photographs and the survey form in the shared drive, in a folder named for the customer.
- ☐ **Send the third message on The install card** to the customer's contact the same day, with the handover sheet attached (its Albanian is a draft: have it read first).
- ☐ **Leave the customer's account:** press **Back to the Greecon console** (the banner's button). It returns you to **Today**.

SAY

Greecon watches your equipment and tells you. The protection built into your equipment remains the safety layer. You will get one message each morning. If there is nothing to do, it says so.

SAY

How alerts reach people: **Act now** *goes by email at once and by text ten minutes later if nobody has acknowledged it; thirty minutes after the alert began, the next person is told by email and text, and so on down the list. Saying you have seen it means pressing the I have seen this link in the message (no sign-in, good for 72 hours) or* **Acknowledge** *on the* **Alerts** *page (for a person with a login).* **Check today** *is one email, held until morning if it is night. Beyond those, three short notes only: one to the people who were told when somebody acknowledges the alert (who took it), one when the problem has stayed clear for 15 minutes (***Resolved***), and one morning message at 07:30 saying whether everything is all right. Quiet hours (22:00 to 07:00) hold everything except Act now.*

STOP

Never promise a saving, a percentage or "AI". Say what Greecon measures and shows. The product shows what the customer's own solar kept on site, at the customer's own prices, from real readings. That is the claim. And say that Greecon is not a safety system.

Their data is theirs. Every reading for the last 31 days, hourly averages for up to a year, the alerts, the audit log and how the account is set up can be downloaded whenever they want, from **Reports** under **Downloads**. If they stop, they can ask Greecon for every reading it holds, as a file.

Handover record

KIT H · HOTEL OR GUESTHOUSE

Field	Answer
Customer and site	
Date, and who was there	
Who is told, in order (name, mobile with country code, email)	
Papers: who signed for the customer, and the date	
Electrician: name and licence number (or: no electrical work was needed)	
Alert limits agreed (tank Critical below, Low below; no-flow level)	
Without a flow meter or the pump's run contact the no-flow alert cannot be raised: said to the owner	☐ Said ☐ Not applicable
Prices entered (electricity, export, water) and where they came from	
Setup list: every step Done and the site Commissioned	☐ Yes
Handover sheet printed and signed	☐ Yes
Shown: Overview, Energy now, Value, Who is told with a live test message, Reports	☐ Yes
Left: label on the box; card with `info@greecon.earth` and your phone	☐ Yes
Photographs and survey form filed in the customer's folder	☐ Yes

Project manager: name and signature

Owner: name and signature

The three most likely problems

What you see	Likely cause	What to do
The solar meter reads zero at midday	A clamp closed on the wrong cable, a closed breaker upstream, or the inverter is limited to zero export	Compare with the meter's own display and test the register from the box (`greecon-edge modbus-test`). Ask the electrician to confirm that the clamps are on the inverter's output phases. If the plant is zero-export, midday solar can honestly be low: check the inverter's display
The tank level is wrong (above 100 percent, below zero, or does not move)	The range or the tank's height was given wrongly; a wire has come off (the module reads 0 and the level reads below zero); a blocked vented cable; or the transmitter is not at the bottom of the tank or not on input 1	Give the ranges again (**Save the ranges**). Check that the transmitter hangs at the bottom with its vented cable free and fixed. Send 4, 12 and 20 mA with the loop calibrator: the module must read 4000, 12000 and 20000
The pump shows running when it is stopped (and the no-flow alert, an Act now, opens while the pump is stopped)	The pump's running contact is inverted	The electrician swaps the contact's normally-open and normally-closed wires, or uses the opposite contact. Until it is right the no-flow alert cannot be trusted

More, by symptom, are in the Appendices of the Complete Deployment Guide (Appendix C) and in the Field Manual. A device that does not answer is, in this order: the converter's address changed (press **Find equipment** again), the number on the device's label not the one on the install card, a wrong speed at the converter, A and B swapped on the data cable, the converter not in gateway mode.
